


Government of Jammu & Kashmir
Skill Development Department Civil Secretariat
Jammu/Srinagar

OM No. DSD-Plan/2/2022-06-SDD (155680)
Dated: 12/04/2022

Subject: Details of works / projects completed during 2021-22 along with geo-tagged photographs for publications of e-book (pictorial compendium) regarding.

In reference to communication received from the Finance Department vide No: FD/DED-II/2022/22/03-FD/153081 dated: 12/03/2022 regarding the subject cited above, the undersigned is directed to enclose here with the requisite information for favour of further necessary action please.


Joint Director (E&S)
Skill Development Department.
A
12/07

Financial Commissioner,
(Additional Chief Secretary)
Finance Department.

Encls: (A/A)

Copy to the:

1. Pvt. Secretary to the Principal Secretary to the Government, Skill Development Department for information of the Principal Secretary.

ITI Sector

FORMAT –“A”

Abstract of works projects physically completed under UT Capex Budget, Loan, Loan,
CSS& PMDP during 2021-22

(Rs. In lakh)

Sr. No.	Source of funds	Total No. of works Physically completed during 2021-22	Total AA cost	Total cost of completion/ expenditure
	Capex Regular	28	649.50	509.05
	Loan Schemes	0	0	0
	CSS	0	0	0
	PMDP/Others	0	0	0
	Total:	28	649.50	509.05

Format – “C”


Geo tagged Photographs of the work (JPG Format with details)




Sr. No.	01
Name of the Work with location	Construction of W/ shop for Motor Mechanic (MMV) / Plumber Trade & auto mobile service Station at IT R.S.Pora
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	93.30
Total cost of completion/ Expdt incurred ending 3/2022	92.78
Date of start (Month/year)	Jul-16
Date of completion (Month/year)	Mar-22
No. of beneficiary	100 trainees



Sr. No.	02
Name of the Work with location	Construction of first floor to ITI building at ITI Nowshera
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	99.90
Total cost of completion/ Expdt incurred ending 3/2022	98.15
Date of start (Month/year)	Sep-19
Date of completion (Month/year)	Mar-22
No. of beneficiary	150

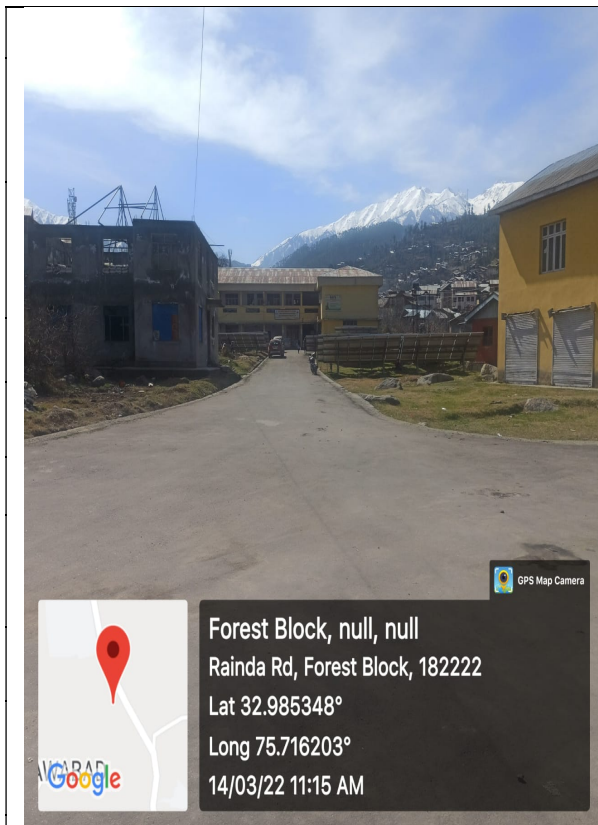

Sr. No.	03
Name of the Work with location	Construction of approach road from Main Gate at ITI Bhaderwah
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Doda
AA Cost (Rs. In lakh)	15.16
Total cost of completion/ Expdt incurred ending 3/2022	15.00
Date of start (Month/year)	Mar-20
Date of completion (Month/year)	Sep-21
No. of beneficiary	400

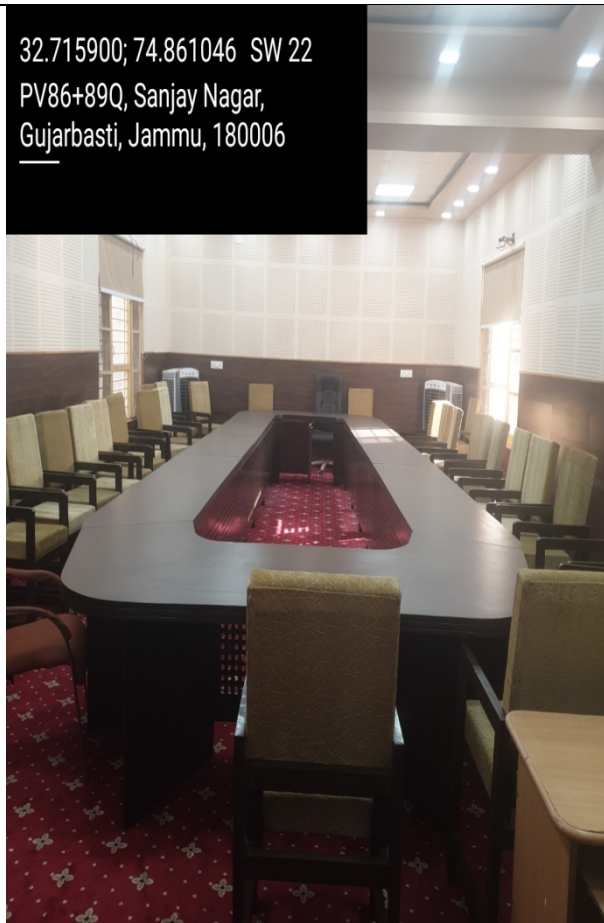


Sr. No.	04
Name of the Work with location	Establishment of Conference Hall at Directorate of Technical Education, Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	JKI
Block/District	Jammu
AA Cost (Rs. In lakh)	14.51
Total cost of completion/ Expdt incurred ending 3/2022	6.00
Date of start (Month/year)	Oct-19
Date of completion (Month/year)	Dec-21
No. of beneficiary	50



Sr. No.	05
Name of the Work with location	Construction of Boundary Wall and Main Gate of Devry Stones at Govt. ITI Kulgam
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	J&K Housing Board
Block/District	Kulgam
AA Cost (Rs. In lakh)	31.57
Total cost of completion/ Expdt incurred ending 3/2022	31.20
Date of start (Month/year)	Jun-20
Date of completion (Month/year)	Mar-22
No. of beneficiary	400




Sr. No.	06
Name of the Work with location	Construction of workshop block at Women ITI, Phase-II Bemina
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	82.58
Total cost of completion/ Expdt incurred ending 3/2022	66.90
Date of start (Month/year)	Jul-20
Date of completion (Month/year)	Jun-21
No. of beneficiary	275

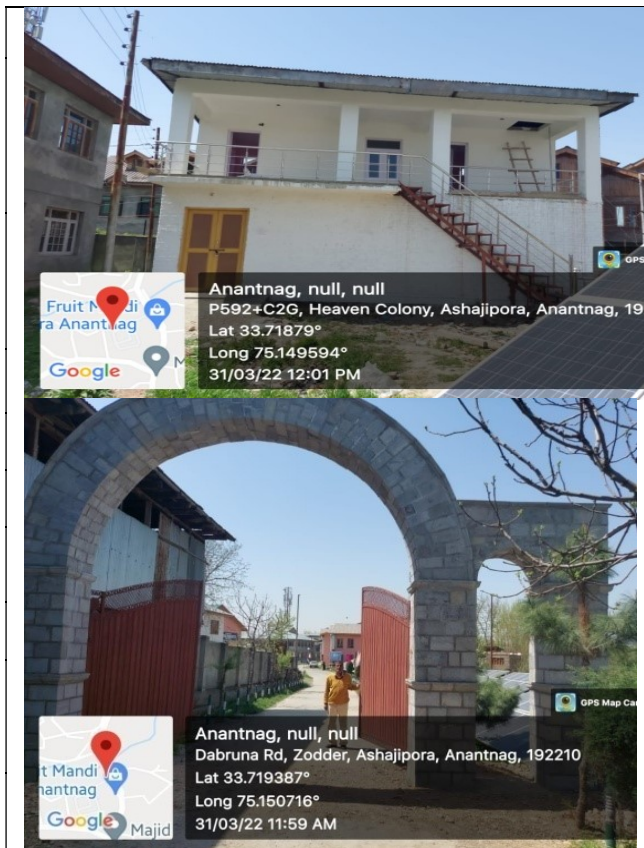

Sr. No.	07
Name of the Work with location	Construction of Chowkidar Qtrs and Main gate with Devri Stones at Govt ITI Anantnag
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Anantnag
AA Cost (Rs. In lakh)	23.91
Total cost of completion/ Expdt incurred ending 3/2022	17.00
Date of start (Month/year)	Sep-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	800 trainees



Sr. No.	08
Name of the Work with location	Macdamization of Internal Roads at Women ITI Bemina
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	10.52
Total cost of completion/ Expdt incurred ending 3/2022	7.80
Date of start (Month/year)	May-21
Date of completion (Month/year)	Aug-21
No. of beneficiary	300

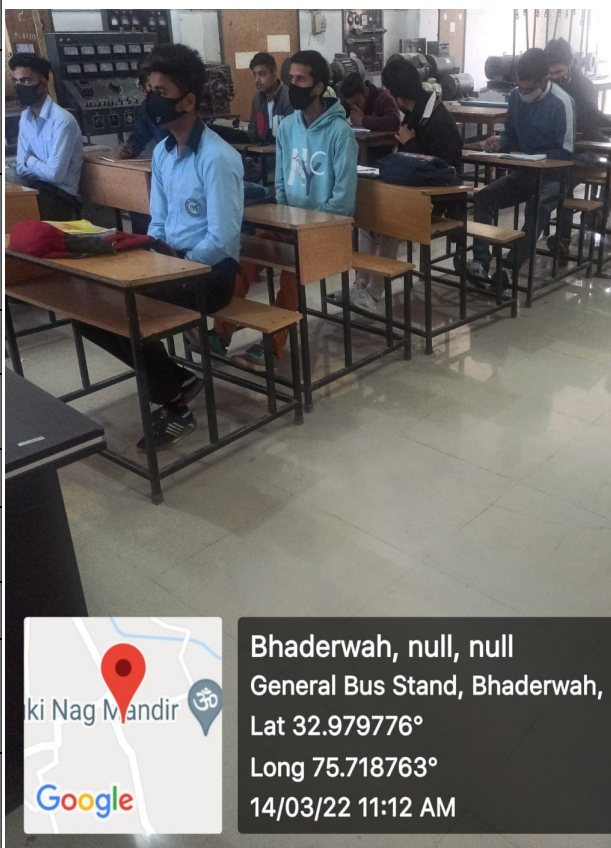


Sr. No.	09
Name of the Work with location	Laying of tiles in various trades Buildings at ITI Bhaderwah
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Doda
AA Cost (Rs. In lakh)	12.00
Total cost of completion/ Exptd incurred ending 3/2022	6.59
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Aug-21
No. of beneficiary	250




Sr. No.	10
Name of the Work with location	Macdamisation of interior roads at Govt. ITI Pampore
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Pulwama
AA Cost (Rs. In lakh)	20.00
Total cost of completion/ Exptd incurred ending 3/2022	12.79
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	300



Sr. No.	11
Name of the Work with location	Construction of workshop block at Women ITI Bemina (Phase III)
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	89.62
Total cost of completion/ Expdt incurred ending 3/2022	60.00
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	275

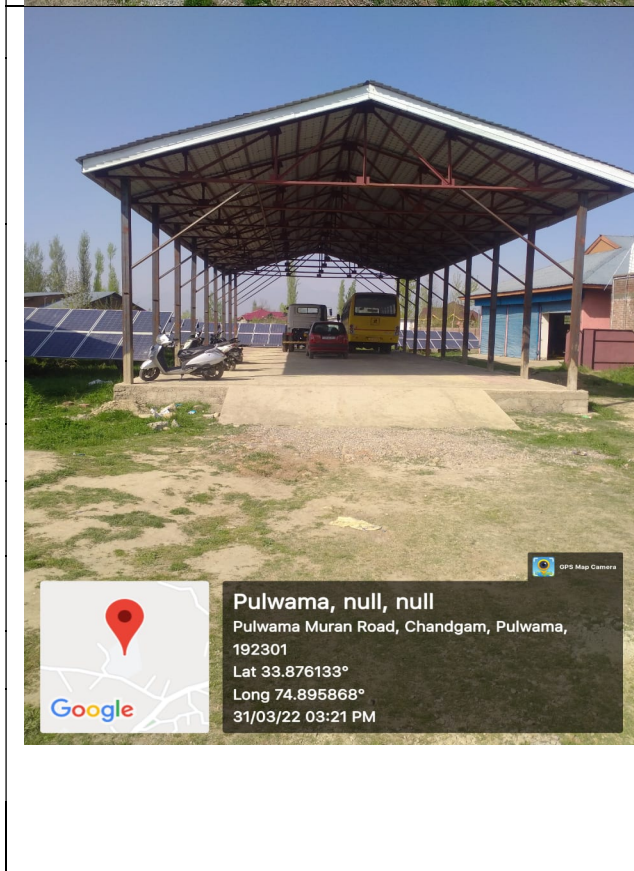

Sr. No.	12
Name of the Work with location	construction of Garage and development of parking area at ITI Pulwama
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Pulwama
AA Cost (Rs. In lakhs)	27.42
Total cost of completion/ Expdt incurred ending 3/2022	15.00
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Dec-21
No. of beneficiary	300

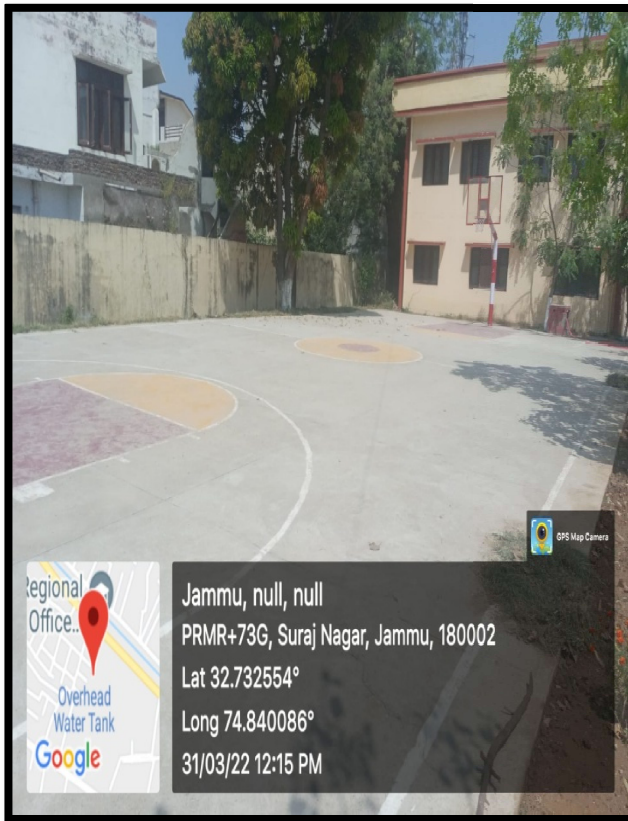


Sr. No.	13
Name of the Work with location	Establishment of Basket ball court at Women ITI Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	10.00
Total cost of completion/ Expdt incurred ending 3/2022	5.00
Date of start (Month/year)	Aug-21
Date of completion (Month/year)	Dec-21
No. of beneficiary	164 trainees



Sr. No.	14
Name of the Work with location	Landscape development of ITI Sopore. Construction of fencing around park proposed in front of administration and women's building
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Baramulla
AA Cost (Rs. In lakh)	3.19
Total cost of completion/ Expdt incurred ending 3/2022	3.05
Date of start (Month/year)	Dec-20
Date of completion (Month/year)	Mar-22
No. of beneficiary	300



Sr. No.	15
Name of the Work with location	Development & Up-gradation of parking area at ITI Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	10.92
Total cost of completion/ Expdt incurred ending 3/2022	10.05
Date of start (Month/year)	Jul-20
Date of completion (Month/year)	Mar-22
No. of beneficiary	900

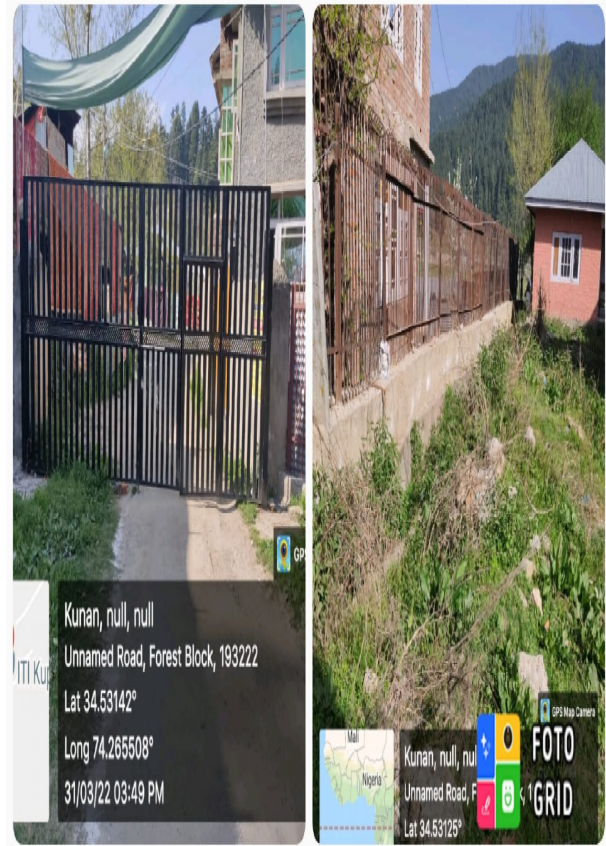

Sr. No.	16
Name of the Work with location	Repair of protection wall & Iron fencing grill at ITI Kupwara
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Kupwara
AA Cost (Rs. In lakh)	6.15
Total cost of completion/ Expdt incurred ending 3/2022	4.95
Date of start (Month/year)	Aug-20
Date of completion (Month/year)	Dec-21
No. of beneficiary	250



Sr. No.	17
Name of the Work with location	White Washing / Face lifting of DSD office at Bikram Chowk Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	2.00
Total cost of completion/ Expdt incurred ending 3/2022	0.97
Date of start (Month/year)	Oct-20
Date of completion (Month/year)	Jun-21
No. of beneficiary	50



Sr. No.	18
Name of the Work with location	Renovation of Hostel Block at ITI building, Shopian
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Shopian
AA Cost (Rs. In lakh)	8.95
Total cost of completion/ Expdt incurred ending 3/2022	6.73
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Feb-22
No. of beneficiary	200



Sr. No.	19
Name of the Work with location	Face lifting of Adm Block & Workshop block at Women ITI Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	11.92
Total cost of completion/ Expdt incurred ending 3/2022	7.42
Date of start (Month/year)	Oct-20
Date of completion (Month/year)	Jan-22
No. of beneficiary	220



Sr. No.	20
Name of the Work with location	Renovation & Construction of Bathrooms (including 1st floor of main block) at ITI Anantnag
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Anantnag
AA Cost (Rs. In lakh)	10.63
Total cost of completion/ Expdt incurred ending 3/2022	6.57
Date of start (Month/year)	Sep-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	800 trainees



Sr. No.	21
Name of the Work with location	Renovation of Ceiling of Stenography Trade & Internal face lifting of Workshops at Women ITI Bemina, Srinagar
Department/ Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	12.33
Total cost of completion/ Expdt incurred ending 3/2022	6.30
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	300



Sr. No.	22
Name of the Work with location	Renovation of Washroom & repair/restoration of Sanitary Disposal System at Women ITI Bemina
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	8.18
Total cost of completion/ Expdt incurred ending 3/2022	3.58
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	300

 <div data-bbox="142 730 743 940">  <p> null, null, null null, null, null, null Long 74.092545° Lat 33.768046° 31/3/2022 02:37 PM </p> </div>	Sr. No.	23
	Name of the Work with location	Repair / Renovation of ITI complex Poonch
	Department// Organisation	Skill Development Department (Directorate of Skill Development)
	Executing Agency	PWD(R&B)
	Block/District	Poonch
	AA Cost (Rs. In lakh)	11.27
	Total cost of completion/ Expdt incurred ending 3/2022	7.42
	Date of start (Month/year)	Jun-21
	Date of completion (Month/year)	Mar-22
	No. of beneficiary	400
 <div data-bbox="142 1648 259 1801"> <p> Latitude: 33.257141 Longitude: 74.831363 Elevation: 2786.6249 m Accuracy: 43.2 m Time: 04-04-2022 12:17 Note: Repair/Whitewash work at Govt Women ITI DHARMARI </p> </div>	Sr. No.	24
	Name of the Work with location	Repair/Whitewash of ITI Dharmari
	Department// Organisation	Skill Development Department (Directorate of Skill Development)
	Executing Agency	PWD(R&B)
	Block/District	Reasi
	AA Cost (Rs. In lakh)	1.61
	Total cost of completion/ Expdt incurred ending 3/2022	1.16
	Date of start (Month/year)	Oct-21
	Date of completion (Month/year)	Mar-22
	No. of beneficiary	150




Sr. No.	25
Name of the Work with location	Repair/Renovation of Office of Joint Director, Skill Development Kashmir, Bemina
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	4.84
Total cost of completion/ Expdt incurred ending 3/2022	2.34
Date of start (Month/year)	Oct-21
Date of completion (Month/year)	Jan-22
No. of beneficiary	30



Sr. No.	26
Name of the Work with location	Repair/Renovation of Office of Joint Director, Skill Development Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	4.63
Total cost of completion/ Expdt incurred ending 3/2022	2.28
Date of start (Month/year)	Oct-21
Date of completion (Month/year)	Jan-22
No. of beneficiary	30



Sr. No.	27
Name of the Work with location	Painting / Colour washing of Women Wing block at ITI Rajouri
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Rajouri
AA Cost (Rs. In lakh)	4.27
Total cost of completion/ Expdt incurred ending 3/2022	2.14
Date of start (Month/year)	Aug-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	550

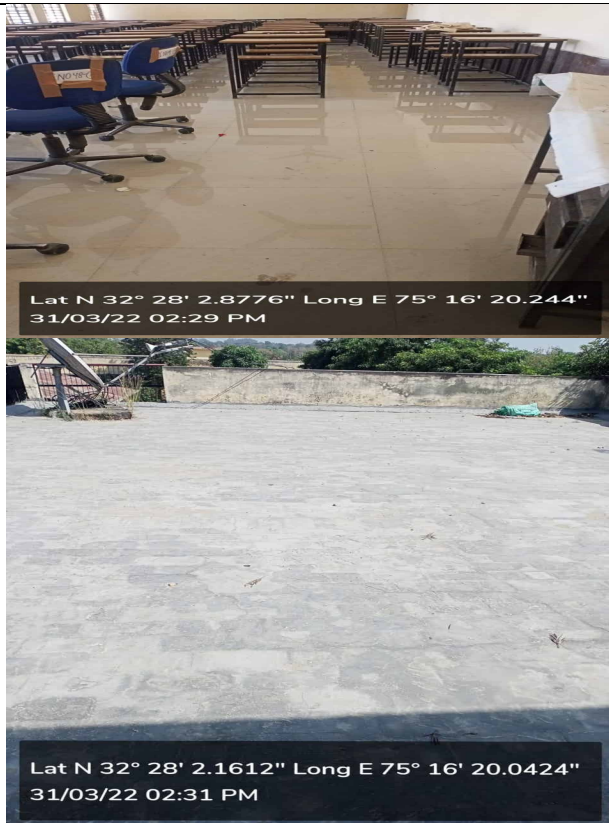

Sr. No.	28
Name of the Work with location	Repair/Renovation of main building, Women Building & Hostel Building at ITI Hiranagar
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD(R&B)
Block/District	Kathua
AA Cost (Rs. In lakh)	18.12
Total cost of completion/ Expdt incurred ending 3/2022	9.88
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	500

Polytechnic Sector

FORMAT –“A”

Abstract of works projects physically completed under UT Capex Budget, Loan, Loan,
CSS& PMDP during 2021-22

(Rs. In lakh)

Sr. No.	Source of funds	Total No. of works Physically completed during 2021-22	Total AA cost	Total cost of completion/ expenditure
	Capex Regular	22	643.97	536.99
	Loan Schemes	0	0	0
	CSS	0	0	0
	PMDP/Others	0	0	0
	Total:	22	643.97	536.99

Format – “C”

Geo tagged Photographs of the work (JPG Format with details)



Sr. No.	01
Name of the Work with location	Const of Cafeteria at Govt Polytechnic Anantnag
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Anantnag
AA Cost (Rs. In lakh)	38.66
Total cost of completion / Expdt incurred ending 3/2022	37.74
Date of start (Month/year)	Mar-19
Date of completion (Month/year)	Dec-21
No. of beneficiary	01 (GP Anantnag)



Sr. No.	02
Name of the Work with location	Establishment of CIIT at Govt. Polytechnic Baramulla
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Baramulla
AA Cost (Rs. In lakh)	405.36
Total cost of completion / Expdt incurred ending 3/2022	398.82
Date of start (Month/year)	Mar-20
Date of completion (Month/year)	Oct-21
No. of beneficiary	350



Sr. No.	03
Name of the Work with location	Construction of compound walling for residential premises of GP Women Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	3.38
Total cost of completion / Expdt incurred ending 3/2022	2.44
Date of start (Month/year)	Apr-21
Date of completion (Month/year)	Dec-21
No. of beneficiary	30



Sr. No.	04
Name of the Work with location	Facelifting of Cafeteria near CIIT, Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	4.00
Total cost of completion / Expdt incurred ending 3/2022	0.89
Date of start (Month/year)	Apr-21
Date of completion (Month/year)	Aug-21
No. of beneficiary	500



Sr. No.	05
Name of the Work with location	Facelifting of Automobile Workshop near CIIT, Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	2.68
Total cost of completion / Expdt incurred ending 3/2022	0.00 (Expdt made by the executing agency from its own resources)
Date of start (Month/year)	Mar-21
Date of completion (Month/year)	Aug-21
No. of beneficiary	500



Sr. No.	06
Name of the Work with location	Construction of 11 KVA Line at Govt. Polytechnic Bandipora
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	KPDCL (JKPDD)
Block/District	Bandipore
AA Cost (Rs. In lakh)	12.60
Total cost of completion / Expdt incurred ending 3/2022	9.45
Date of start (Month/year)	Aug-21
Date of completion (Month/year)	Dec-21
No. of beneficiary	310



Sr. No.	07
Name of the Work with location	11KVA Power Supply to Govt. Polytechnic Larkipora Anantnag.
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	KPDCL (JKPDD)
Block/District	Anantnag
AA Cost (Rs. In lakh)	10.89
Total cost of completion / Expdt incurred ending 3/2022	0.00 (Expdt made by the executing agency from its own resources)
Date of start (Month/year)	Aug-21
Date of completion (Month/year)	Feb-22
No. of beneficiary	01 (GP Anantnag)




Sr. No.	08
Name of the Work with location	Installation of 04 No. Collapsible Doors at Govt. Polytechnic Kulgam.
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Kulgam
AA Cost (Rs. In lakh)	4.00
Total cost of completion / Expdt incurred ending 3/2022	2.60
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Jun-21
No. of beneficiary	01 (GP Kulgam)




Sr. No.	09
Name of the Work with location	Creation of 250 Kva Distribution SubStation at Govt Polytechnic Udhampur
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	JPDCL (JKPDD)
Block/District	Udhampur
AA Cost (Rs. In lakh)	30.99
Total cost of completion / Expdt incurred ending 3/2022	7.05
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Jan-22
No. of beneficiary	300




Sr. No.	10
Name of the Work with location	Installation of 400 Kva Sub station along with HT LT Network for Govt Polytechnic Shopian
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	KPDCL (JKPDD)
Block/District	Shopian
AA Cost (Rs. In lakh)	12.24
Total cost of completion / Expdt incurred ending 3/2022	9.18
Date of start (Month/year)	Jun-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	500

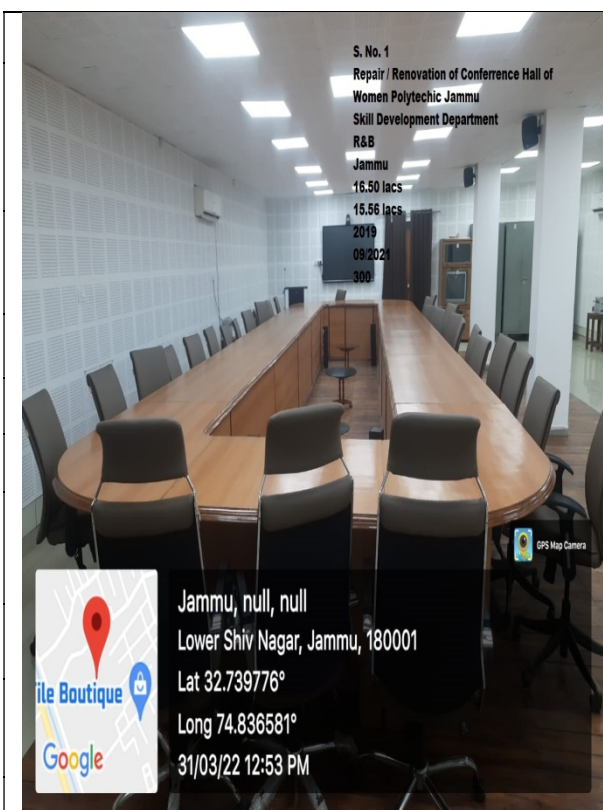


Sr. No.	11
Name of the Work with location	Repair/Renovation of Conference Hall of Women Polytechnic Jammu.
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	16.53
Total cost of completion / Expdt incurred ending 3/2022	15.45
Date of start (Month/year)	Jun-19
Date of completion (Month/year)	Sep-21
No. of beneficiary	300

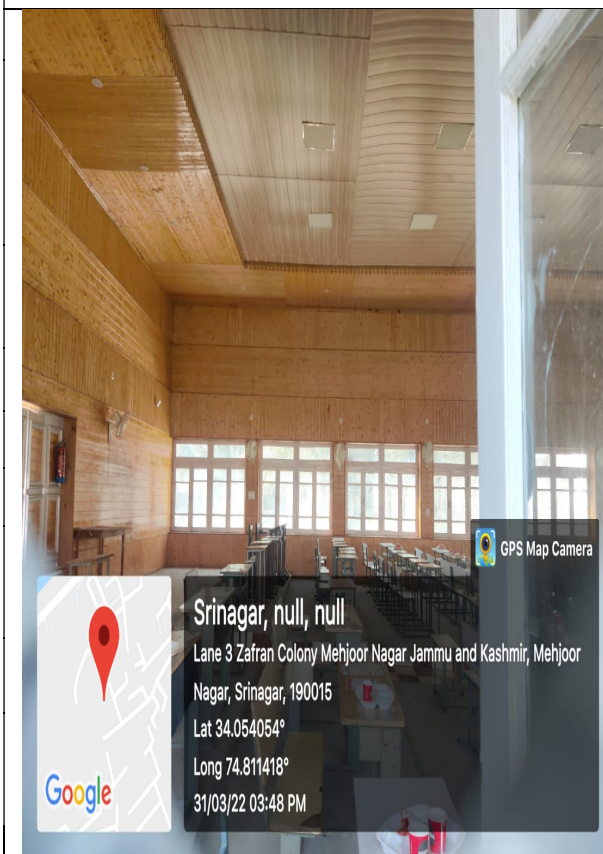

Sr. No.	12
Name of the Work with location	Civil Work of Auditorium at KGP Srinagar including painting/ polishing at Kashmir Govt Polytechnic.
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	10.35
Total cost of completion / Expdt incurred ending 3/2022	1.53
Date of start (Month/year)	Jun-20
Date of completion (Month/year)	Mar-22
No. of beneficiary	1000

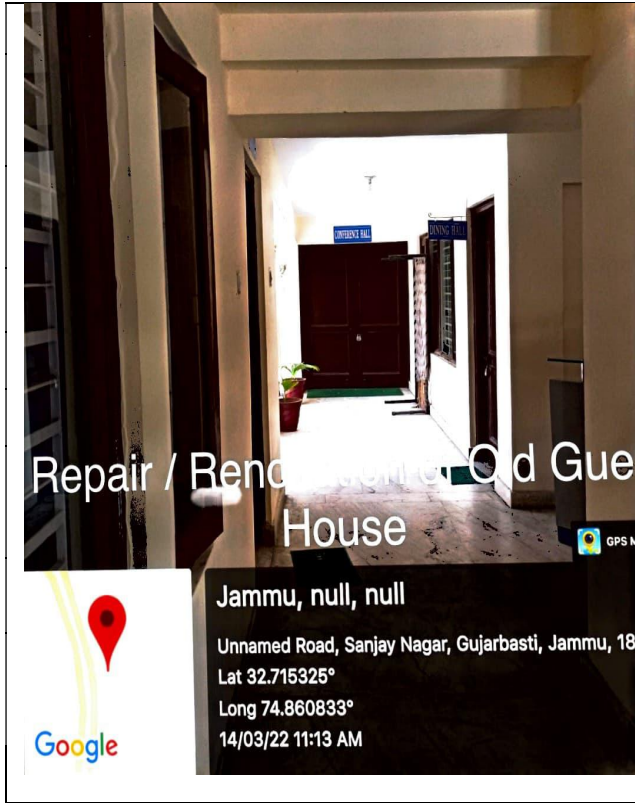


Sr. No.	13
Name of the Work with location	Repair /Renovation of old Guest House at Govt. Polytechnic Boys Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	6.70
Total cost of completion / Expdt incurred ending 3/2022	4.26
Date of start (Month/year)	Mar-21
Date of completion (Month/year)	Aug-21
No. of beneficiary	20

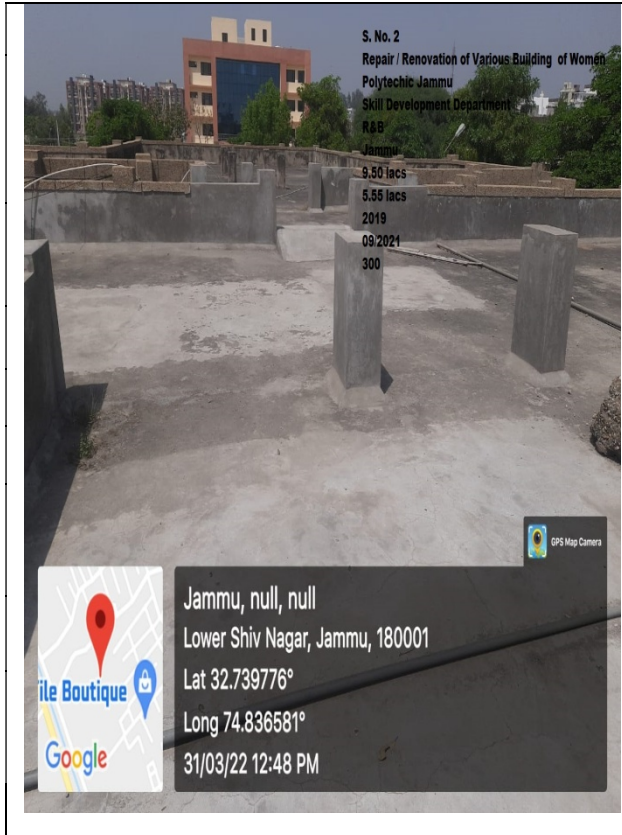


Sr. No.	14
Name of the Work with location	Repair /Renovation of various buildings at Govt. women Polytechnic Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	7.17
Total cost of completion / Expdt incurred ending 3/2022	5.55
Date of start (Month/year)	Mar-21
Date of completion (Month/year)	Sep-21
No. of beneficiary	300



Sr. No.	15
Name of the Work with location	Repair / Renovation of Civil & Electrical Engg. Wing at Govt Polytechnic Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	10.00
Total cost of completion / Expdt incurred ending 3/2022	4.18
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	1000

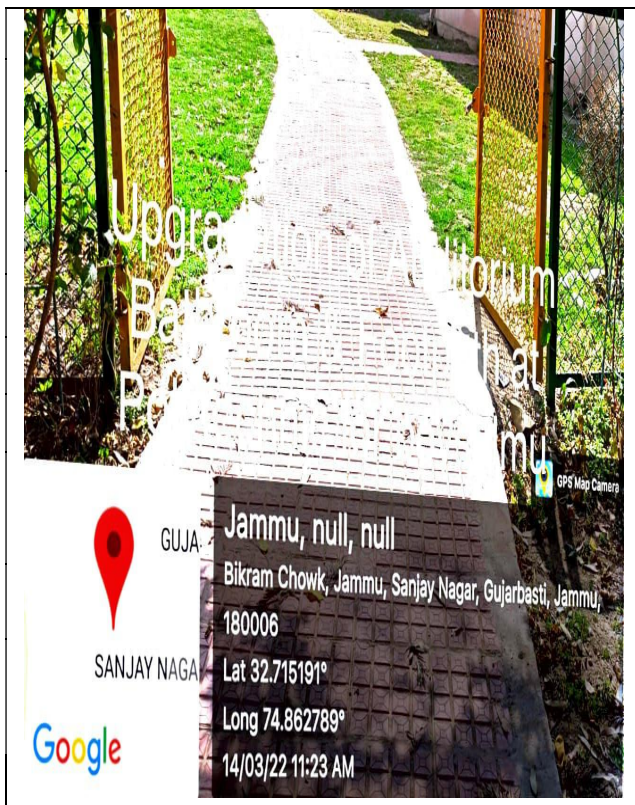

Sr. No.	16
Name of the Work with location	Repair / Renovation of Auditorium Bathroom at Govt Polytechnic Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	7.00
Total cost of completion / Expdt incurred ending 3/2022	3.17
Date of start (Month/year)	Aug-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	200

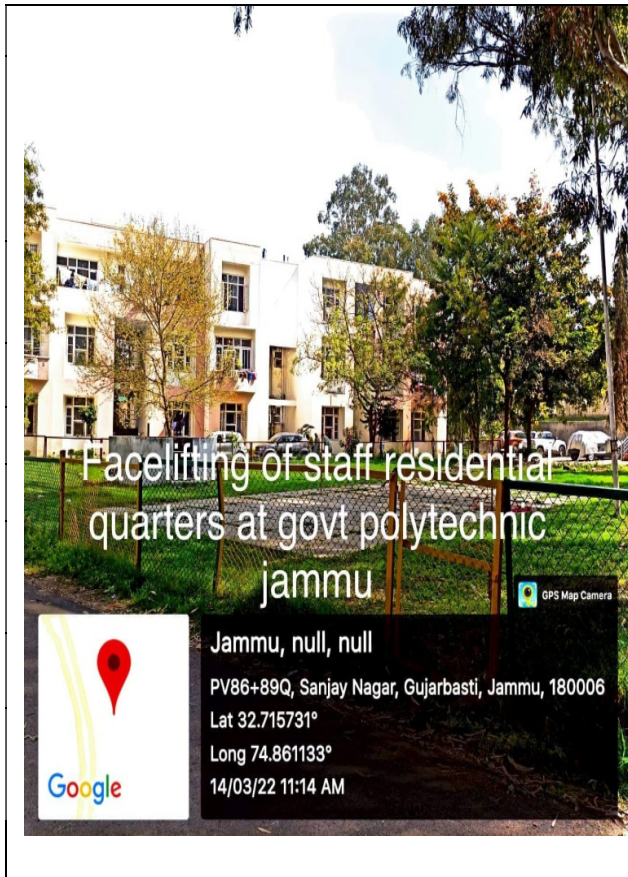


Sr. No.	17
Name of the Work with location	Repair/Renovation/Facelighting of Staff Residential Quarters at Govt Polytechnic Jammu
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	10.00
Total cost of completion / Expdt incurred ending 3/2022	3.93
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	20



Sr. No.	18
Name of the Work with location	Repair / Renovation of DSD Office Jammu (including Flooring, Bathrooms, Roof tiling, Paint etc.)
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Jammu
AA Cost (Rs. In lakh)	15.00
Total cost of completion / Expdt incurred ending 3/2022	7.42
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	45




Sr. No.	19
Name of the Work with location	Repair/Renovation of Bathrooms at CDI (Craft Development Institute) Srinagar
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	4.31
Total cost of completion / Expdt incurred ending 3/2022	2.36
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Oct-21
No. of beneficiary	20

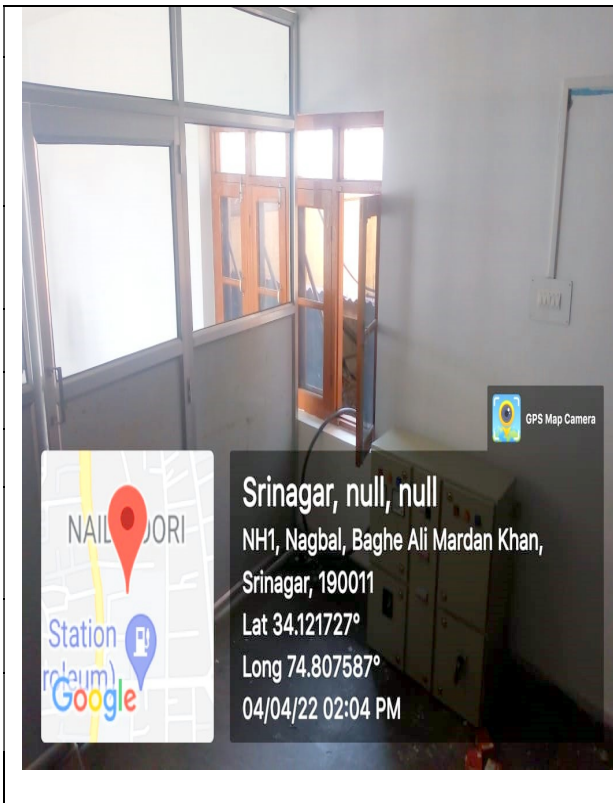

Sr. No.	20
Name of the Work with location	Repair/Renovation of Hostel at CDI (Craft Development Institute) Srinagar
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	14.18
Total cost of completion / Expdt incurred ending 3/2022	7.51
Date of start (Month/year)	Jul-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	20



Sr. No.	21
Name of the Work with location	Establishment of Conference Hall at Directorate of Technical Education, Srinagar.
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	PWD (R&B)
Block/District	Srinagar
AA Cost (Rs. In lakh)	16.58
Total cost of completion / Expdt incurred ending 3/2022	12.44
Date of start (Month/year)	Mar-21
Date of completion (Month/year)	Mar-22
No. of beneficiary	45

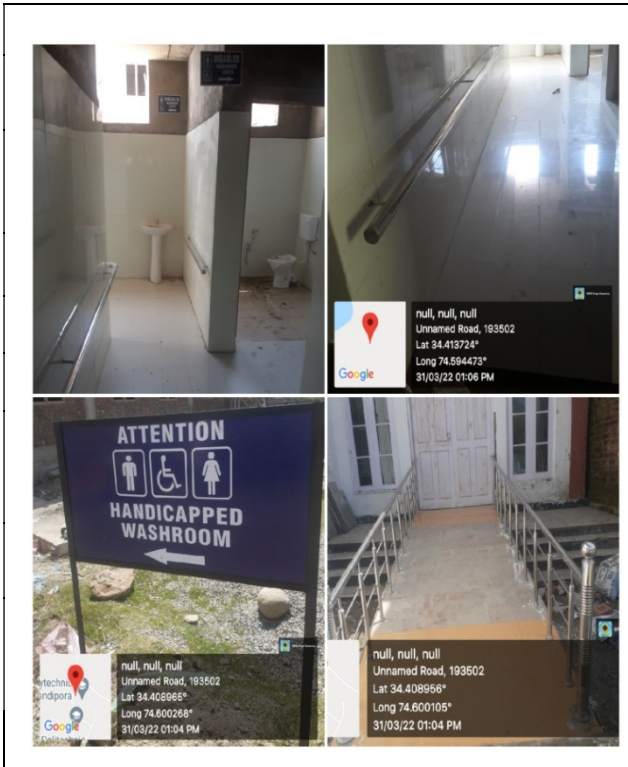

Sr. No.	22
Name of the Work with location	Constr of PWD bathroom (M/F) at GP Bandipore
Department// Organisation	Skill Development Department (Directorate of Skill Development)
Executing Agency	JKPCC
Block/District	Bandipore
AA Cost (Rs. In lakh)	1.35
Total cost of completion / Expdt incurred ending 3/2022	1.02
Date of start (Month/year)	Feb-22
Date of completion (Month/year)	Mar-22
No. of beneficiary	06

